

DRAFT FOR DISCUSSION PURPOSES - INFORMATION AS OF 05/13/02


ID	Task Name	% Complete	Duration	Start	Finish	Predecessors	2002											
							Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
1	Long Term Exposure Study: EHC (EHCJL/02/02)	10%	536 days	Thu 11/1/01	Thu 11/20/03													
2	Investigator Brochure	100%	15 days	Thu 11/1/01	Wed 11/21/01													
3	Study Objectives	100%	5 days	Thu 11/1/01	Wed 11/7/01													
4	Summary Plan	100%	46 days	Thu 11/8/01	Thu 1/10/02	3												
5	Site Selection	100%	0 days	Thu 1/10/02	Thu 1/10/02	4												
6	Questionnaire Development	100%	35 days	Fri 1/11/02	Thu 2/28/02	4												
7	Protocol Development	100%	82 days	Fri 1/11/02	Mon 5/6/02	2,4												
8	Final Draft Protocol, Informed Consent	100%	0 days	Mon 5/6/02	Mon 5/6/02	7,8												
9	IRB Review	100%	1 day	Tue 5/7/02	Tue 5/7/02	8												
10	IRB Approval	100%	0 days	Tue 5/7/02	Tue 5/7/02	9												
11	Final Protocol, Informed Consent	100%	0 days	Tue 5/7/02	Tue 5/7/02	10												
12	Bioanalytical Methods Setup	0%	80 days	Fri 1/11/02	Thu 5/2/02	4												
13	Project Agreement (protocol, study execution)	0%	15 days	Tue 5/7/02	Mon 5/27/02	8												
14	Recruitment and Screening	0%	19 days	Mon 5/13/02	Thu 6/6/02													
15	Recruitment and Screening (Lincoln)	0%	7 days	Mon 5/13/02	Tue 6/2/02													
16	Recruitment and Screening (Phoenix)	0%	3 days	Tue 6/4/02	Thu 6/6/02													
17	Test Cigarettes Available	0%	0 days	Wed 5/1/02	Wed 5/1/02													
18	Test Cigarettes Delivered (Lincoln)	0%	1 day	Fri 5/17/02	Fri 5/17/02													
19	Test Cigarettes Delivered (Phoenix)	0%	1 day	Thu 5/23/02	Thu 5/23/02													
20	Data analysis plan	0%	25 days	Tue 5/7/02	Mon 6/10/02	6												
21	Clinical Testing	0%	276 days	Fri 5/31/02	Sun 6/22/03													
22	Clinical Performance (Lincoln)	0%	271 days	Fri 5/31/02	Fri 6/13/03	15,18												
23	Clinical Performance (Phoenix)	0%	268 days	Fri 6/14/02	Sun 6/22/03	16,19												
24	Lab Analysis	0%	295 days	Fri 5/31/02	Thu 7/17/03	12,21SS												
25	Data Management	0%	315 days	Fri 5/31/02	Thu 8/14/03	21SS												
26	Data Analysis	0%	315 days	Fri 6/14/02	Thu 8/28/03	25SS+10 days												
27	Draft exposure report (3 months)	0%	25 days	Fri 11/1/02	Thu 12/5/02	21SS+110 days												
28	PM review of draft exposure report (3 months)	0%	20 days	Fri 12/6/02	Thu 1/2/03	27												
29	3 month results available to PM	0%	0 days	Fri 1/3/03	Fri 1/3/03	28												
30	Draft 12 month report	0%	20 days	Fri 8/29/03	Thu 9/25/03	26												
31	PM Review of draft report	0%	20 days	Fri 9/26/03	Thu 10/23/03	30												
32	12 month results available	0%	0 days	Thu 10/23/03	Thu 10/23/03	31												
33	Final 12 month report	0%	20 days	Fri 10/24/03	Thu 11/20/03	32												
34	Final Results	0%	0 days	Thu 11/20/03	Thu 11/20/03	133												

check MDS info

Project: Long Term
Date: Thu 5/23/02

Task
Split
Progress

Milestone
Summary
Rolled Up Task



Rolled Up Split
Rolled Up Milestone
Rolled Up Progress

External Tasks
Project Summary
External Milestone

Deadline



PM3006787560

DRAFT FOR DISCUSSION PURPOSES - INFORMATION AS OF 05/13/02


ID	Task Name	% Complete	Duration	Start	Finish	Predecessors	2003												2004	
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
1	Long Term Exposure Study: EHC (EHCJL/02/02)	10%	536 days	Thu 11/1/01	Thu 11/28/03															
2	Investigator Brochure	100%	15 days	Thu 11/1/01	Wed 11/21/01															
3	Study Objectives	100%	5 days	Thu 11/1/01	Wed 11/7/01															
4	Summary Plan	100%	46 days	Thu 11/8/01	Thu 1/10/02	3														
5	Site Selection	100%	0 days	Thu 1/10/02	Thu 1/10/02	4														
6	Questionnaire Development	100%	35 days	Fri 1/11/02	Thu 2/28/02	4														
7	Protocol Development	100%	82 days	Fri 1/11/02	Mon 5/6/02	2,4														
8	Final Draft Protocol, Informed Consent	100%	0 days	Mon 5/6/02	Mon 5/6/02	7,6														
9	IRB Review	100%	1 day	Tue 5/7/02	Tue 5/7/02	8														
10	IRB Approval	100%	0 days	Tue 5/7/02	Tue 5/7/02	9														
11	Final Protocol, Informed Consent	100%	0 days	Tue 5/7/02	Tue 5/7/02	10														
12	Bioanalytical Methods Setup	0%	80 days	Fri 1/11/02	Thu 5/2/02	4														
13	Project Agreement (protocol, study execution)	0%	15 days	Tue 5/7/02	Mon 5/27/02	8														
14	Recruitment and Screening	0%	19 days	Mon 5/13/02	Thu 6/6/02															
15	Recruitment and Screening (Lincoln)	0%	7 days	Mon 5/13/02	Tue 5/21/02															
16	Recruitment and Screening (Phoenix)	0%	3 days	Tue 6/4/02	Thu 6/6/02															
17	Test Cigarettes Available	0%	0 days	Wed 5/1/02	Wed 5/1/02															
18	Test Cigarettes Delivered (Lincoln)	0%	1 day	Fri 5/17/02	Fri 5/17/02															
19	Test Cigarettes Delivered (Phoenix)	0%	1 day	Thu 5/23/02	Thu 5/23/02															
20	Data analysis plan	0%	25 days	Tue 5/7/02	Mon 6/10/02	16														
21	Clinical Testing	0%	276 days	Fri 5/31/02	Sun 6/22/03															
22	Clinical Performance (Lincoln)	0%	271 days	Fri 5/31/02	Fri 6/13/03	15,18														
23	Clinical Performance (Phoenix)	0%	266 days	Fri 6/14/02	Sun 6/22/03	18,19														
24	Lab Analysis	0%	295 days	Fri 5/31/02	Thu 7/17/03	12,21SS														
25	Data Management	0%	315 days	Fri 5/31/02	Thu 8/14/03	21SS														
26	Data Analysis	0%	315 days	Fri 6/14/02	Thu 6/28/03	25SS+10 days														
27	Draft exposure report (3 months)	0%	25 days	Fri 11/1/02	Thu 12/5/02	21SS+110 days														
28	PM review of draft exposure report (3 months)	0%	20 days	Fri 12/6/02	Thu 1/2/03	27														
29	3 month results available to PM	0%	0 days	Fri 1/3/03	Fri 1/3/03	28														
30	Draft 12 month report	0%	20 days	Fri 8/29/03	Thu 9/25/03	26														
31	PM Review of draft report	0%	20 days	Fri 9/26/03	Thu 10/23/03	30														
32	12 month results available	0%	0 days	Thu 10/23/03	Thu 10/23/03	31														
33	Final 12 month report	0%	20 days	Fri 10/24/03	Thu 11/20/03	32														
34	Final Results	0%	0 days	Thu 11/20/03	Thu 11/20/03	33														

Project: Long Term
Date: Thu 5/23/02Task
Split
ProgressMilestone
Summary
Rolled Up TaskRolled Up Split
Rolled Up Milestone
Rolled Up ProgressExternal Tasks
Project Summary
External Milestone

Deadline

PM3006787561

DRAFT FOR DISCUSSION PURPOSES - INFORMATION AS OF 04/10/02

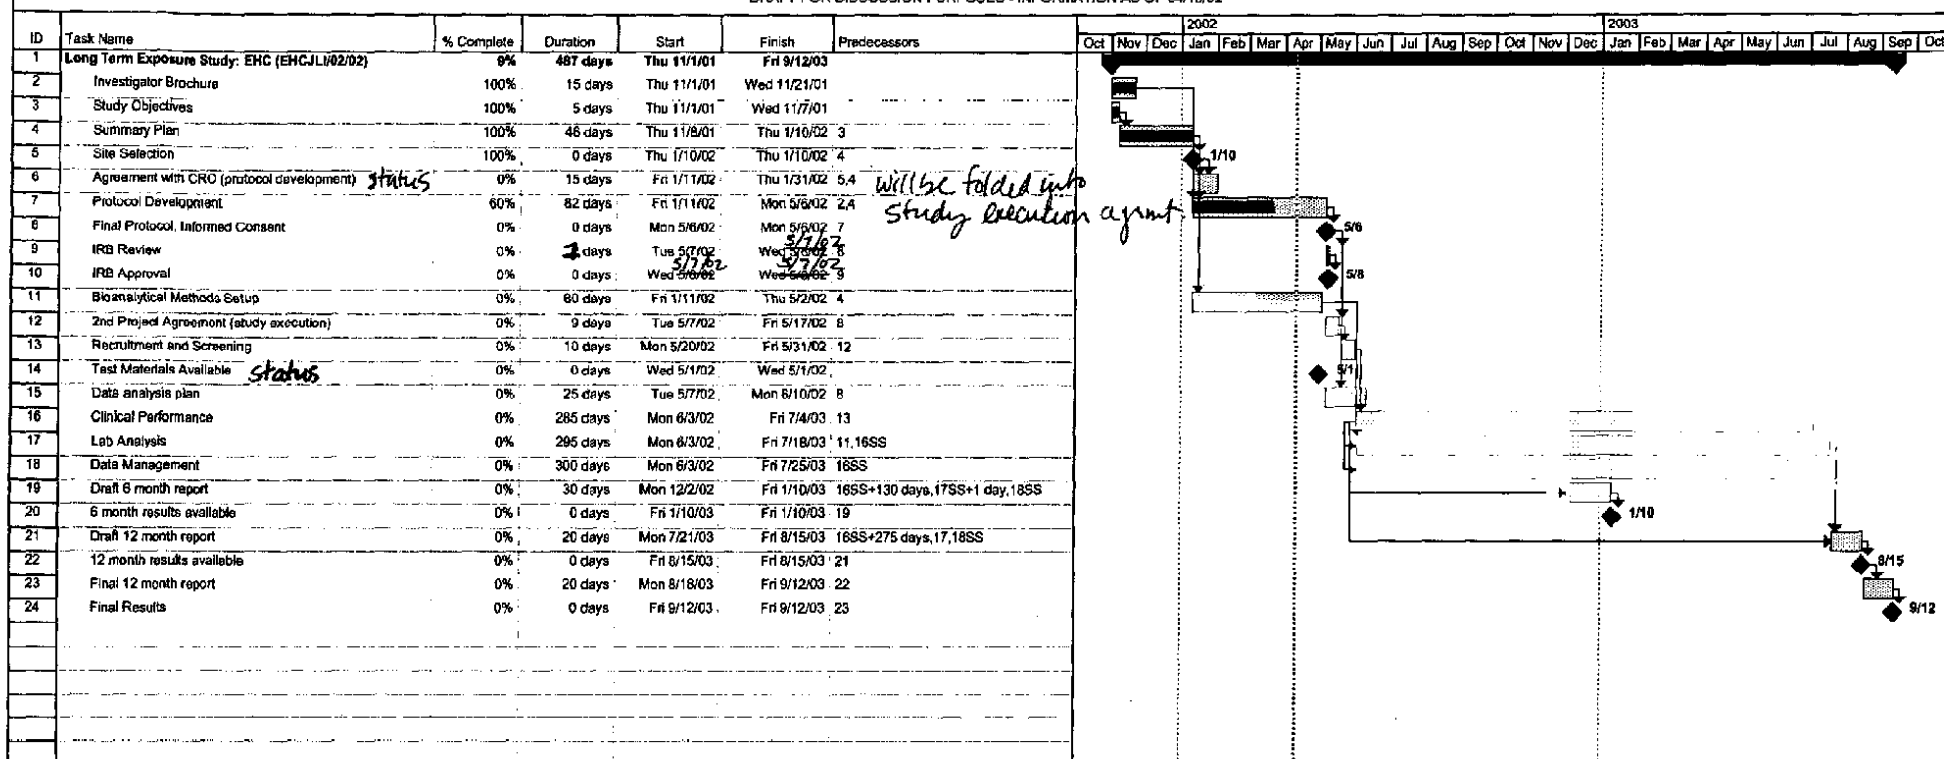

Recruitment + screening site 1: 5/13-5/21

Recruitment + screening site 2: 6/4-6/6

~~Recruitment + screening site 3: 5/20-6/5~~ [changing since Neptune not being used?]

Clinical Performance site 1: 5/31/02-6/13/03

clinical Performance site 2: 6/14/02-6/22/03

~~clinical performance site 3: 6/7/02-6/20/03~~ [changing since Neptune not being used?]

? Add Amer analysis?

Product shipped on 5/17/02

Project: Long Term
Date: Wed 4/10/02

Task

Split

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Split

Rolled Up Milestone

Rolled Up Progress

External Tasks

Project Summary

External Milestone

Deadline
